



Coogee Single Asset Trust

ABN 70 131 039 110

Project Update

June 2022

Anden Coogee Apartments



Date: 28 June 2022

Prepared by: HCAP Asset Management

Project Name: Anden Coogee Apartments

Project Address: 190-192 Oberon St, Coogee NSW 2034

Construction Commencement: August 2020

Anticipated Completion: Late Q3 / Q4 2022

Construction Update

Builder's report to 2nd June 2022:


Since the decline in rain fall, the bulk excavation on the civil works area has begun and upstands in the landscaping area have been formed, reinforcement installed, and poured with concrete on 01/06/2022. Stripping of the landscaping area commenced on 02/06/2022 which will now enable the landscape subcontractor to begin bulk filling of the landscape areas in due course.

Joinery install recommenced in apartments G02 and 104 on 02/06/2022 with apartment G01 and 104 kitchen finalising on 06/06/2022. As for majority of remaining apartments, shop drawings are complete and we are expecting for construction drawings to be issued within the coming days.

Façade restoration has progressed quite steadily considering the inclement weather recently experienced on the project. The main structural components of the façade restoration such as shelf angles supports, ResiTie remedial wall locking, and lintels for window and door openings has been completed. The aluminium window replacements have also commenced with the Eastern elevation now complete. As for final remedial works, repointing has commenced on both Eastern and Northern elevations, due for completion end of June 2022.



North-West Façade: Crane removed and view of masonry, aluminium cladding, and class 2 off-form concrete works

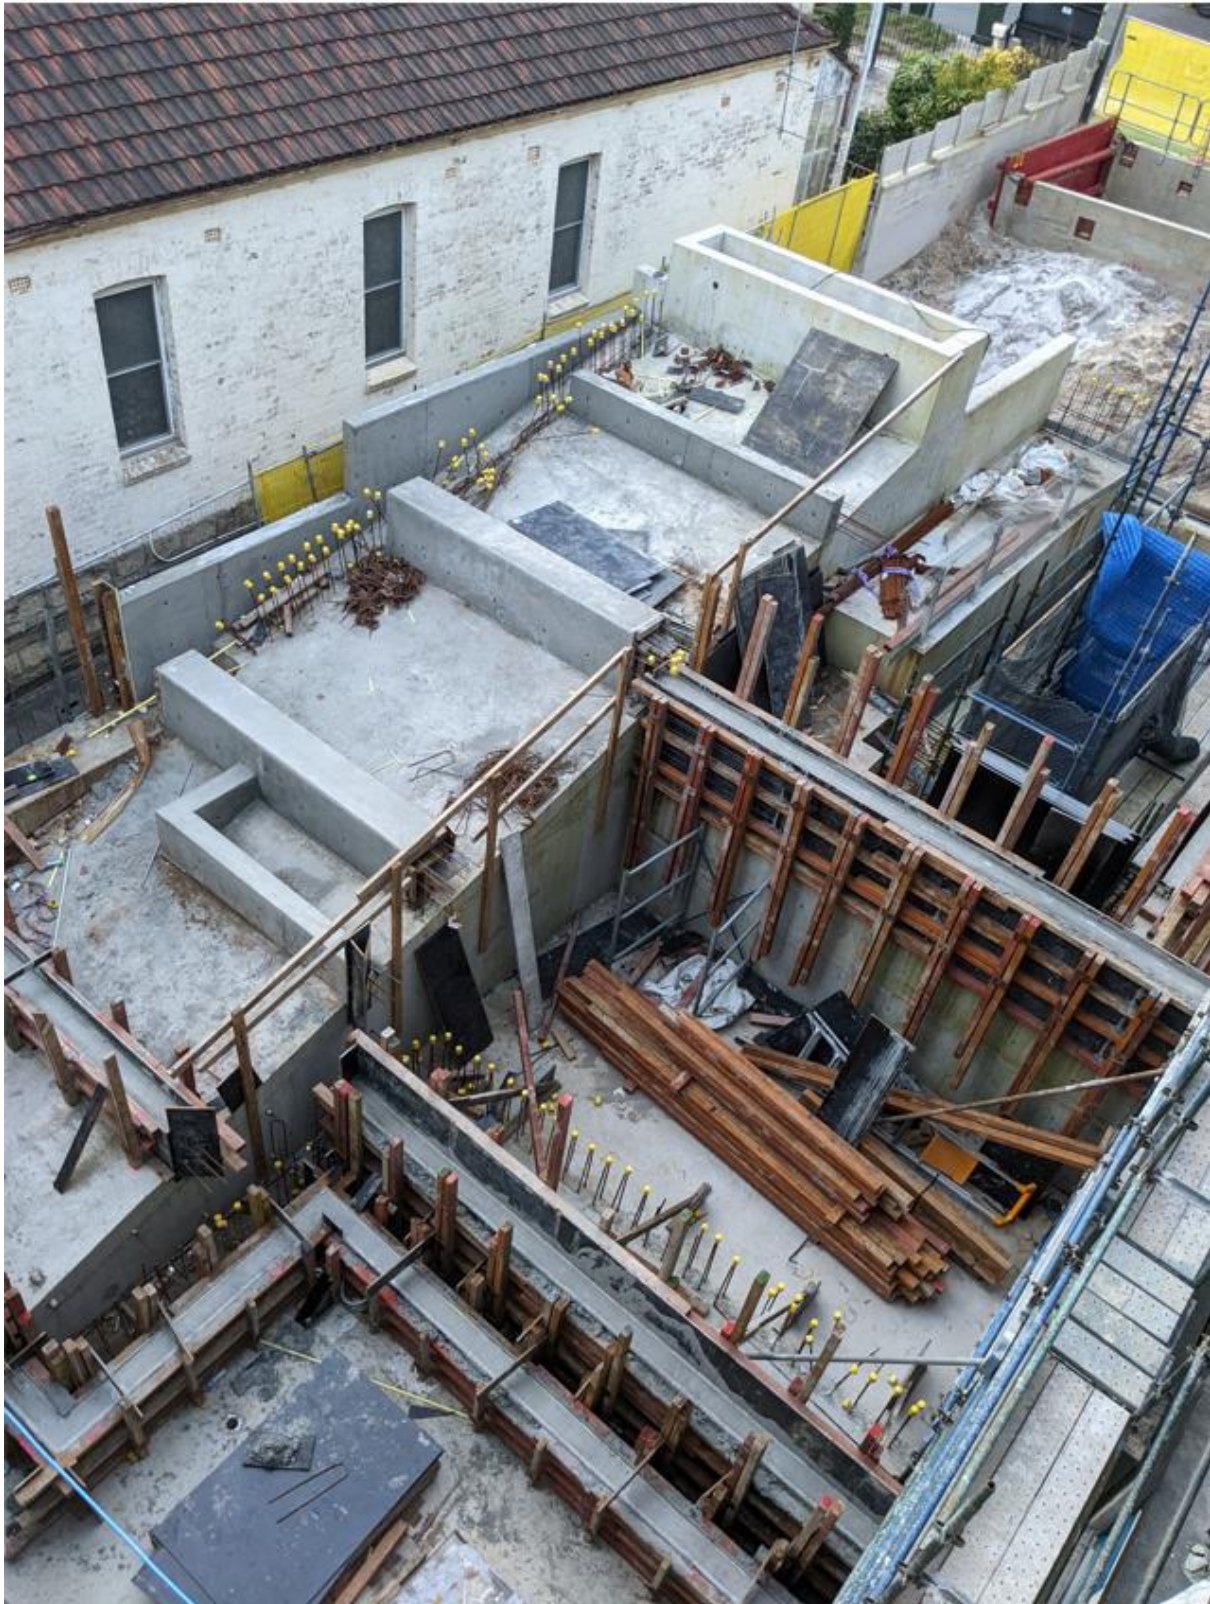

Western elevation: Concrete upstands in the Communal Open Space



Northern elevation Level 1 to Level 2: Repointing of the Retained Facade



Apartment 104: Joinery delivery ready for installation



Anden"



